

PUBLIC INFORMATION BULLETIN NO. 23
AUGUST - SEPTEMBER 2020
AWA STREET WASTEWATER PUMP STATION
FORCE MAIN AND SEWER SYSTEM IMPROVEMENTS
WAIAKAMILO ROAD TRUNK SEWER
JOB NO. W5-16

GENERAL INFORMATION

This bulletin is published to the project website (www.awasewer.org) monthly to keep the community informed about construction work associated with the Awa Street Wastewater Pump Station Force Main and Sewer Improvements – Waiakamilo Road Trunk Sewer Project. The contract Notice-To-Proceed was issued to FV Coluccio Construction Company (FVCCC) on June 27, 2018. Heavy construction is scheduled to continue through the Summer of 2021. Please refer to the attached map and visit the project website for more detailed information about this project. To request hard copies of the monthly information bulletins please call the project hotline at (808) 219-7009.

UPDATES FOR ONGOING ACTIVITIES

FVCCC performed the following work in July:

- Pre-drilling and jet grouting for construction of microtunneling shafts and pipe and manhole excavations.
- Construction of microtunneling and manhole installation shafts.
- Installation of new sewer lines by open trenching, including trench restoration.
- Finishing of the interiors of newly installed manholes.
- Restoration of curbs and pavement.

AUGUST – SEPTEMBER FORECAST OF ACTIVITIES

The activities listed below are scheduled to continue and/or begin in August and/or September. The approximate locations and work hours for these activities are shown on the attached map.

- Relocation of underground and overhead utilities.
- Pre-excavation of underground obstructions.
- Pre-drilling and jet grouting for construction of microtunneling shafts.

- Construction of microtunneling and manhole installation shafts, including installation of sheetpiles.
- Installation of new sewer lines by microtunneling.
- Restoration of landscaping, curbs, and pavement.

TRAFFIC UPDATES FOR AUGUST – SEPTEMBER

Construction work will require relatively isolated lane closures at several locations on Waiakamilo Rd., Houghtailing St., Dillingham Blvd., and/or Nimitz Hwy. Access to driveways will be maintained via right turn motions from the travel lanes fronting them; however, access to some driveways via left turn motions may not be available due to the presence of work area closures.

Along Waiakamilo Rd., continuous daytime and nighttime work is anticipated to occur. On Nimitz Hwy., near the intersection with Waiakamilo Rd., work is anticipated to occur during nighttime hours on the weekdays and all day on the weekends.

Detours may be involved with work located within or near the intersections of Nimitz Hwy. and Dillingham Blvd. See below for associated traffic detours.

- **Traffic Detour for Work near Nimitz Hwy.**
6:00 pm to 2:00 am, Intermittently Monday through Saturday
Through and left turn movements out of Piers 39 and 40 towards Waiakamilo Rd. and Nimitz Hwy. may be prohibited and detoured via right turn and U-turn on Nimitz Hwy.

Left turn movements from Waiakamilo Rd. towards Nimitz Hwy. eastbound; and through movements from Waiakamilo Rd. to Piers 39 and 40 may be prohibited and detoured via Kalani St. and Kalihi St.

Left turn movements from Nimitz Hwy. towards Waiakamilo Rd. and Piers 39 and 40 may be prohibited and detoured via U-turns on Nimitz Hwy near Pier 38 and Libby Street, respectively.

CONTACT INFORMATION


For more information about this project, please visit the project website: www.awasewer.org or call the project hotline at (808) 219-7009.

CONSTRUCTION ACTIVITIES SCHEDULED FOR AUGUST - SEPTEMBER 2020

54" PIPE INSTALLATION BY OPEN EXCAVATION

54" PIPE INSTALLATION BY MICROTUNNELING

42" PIPE INSTALLATION BY MICROTUNNELING

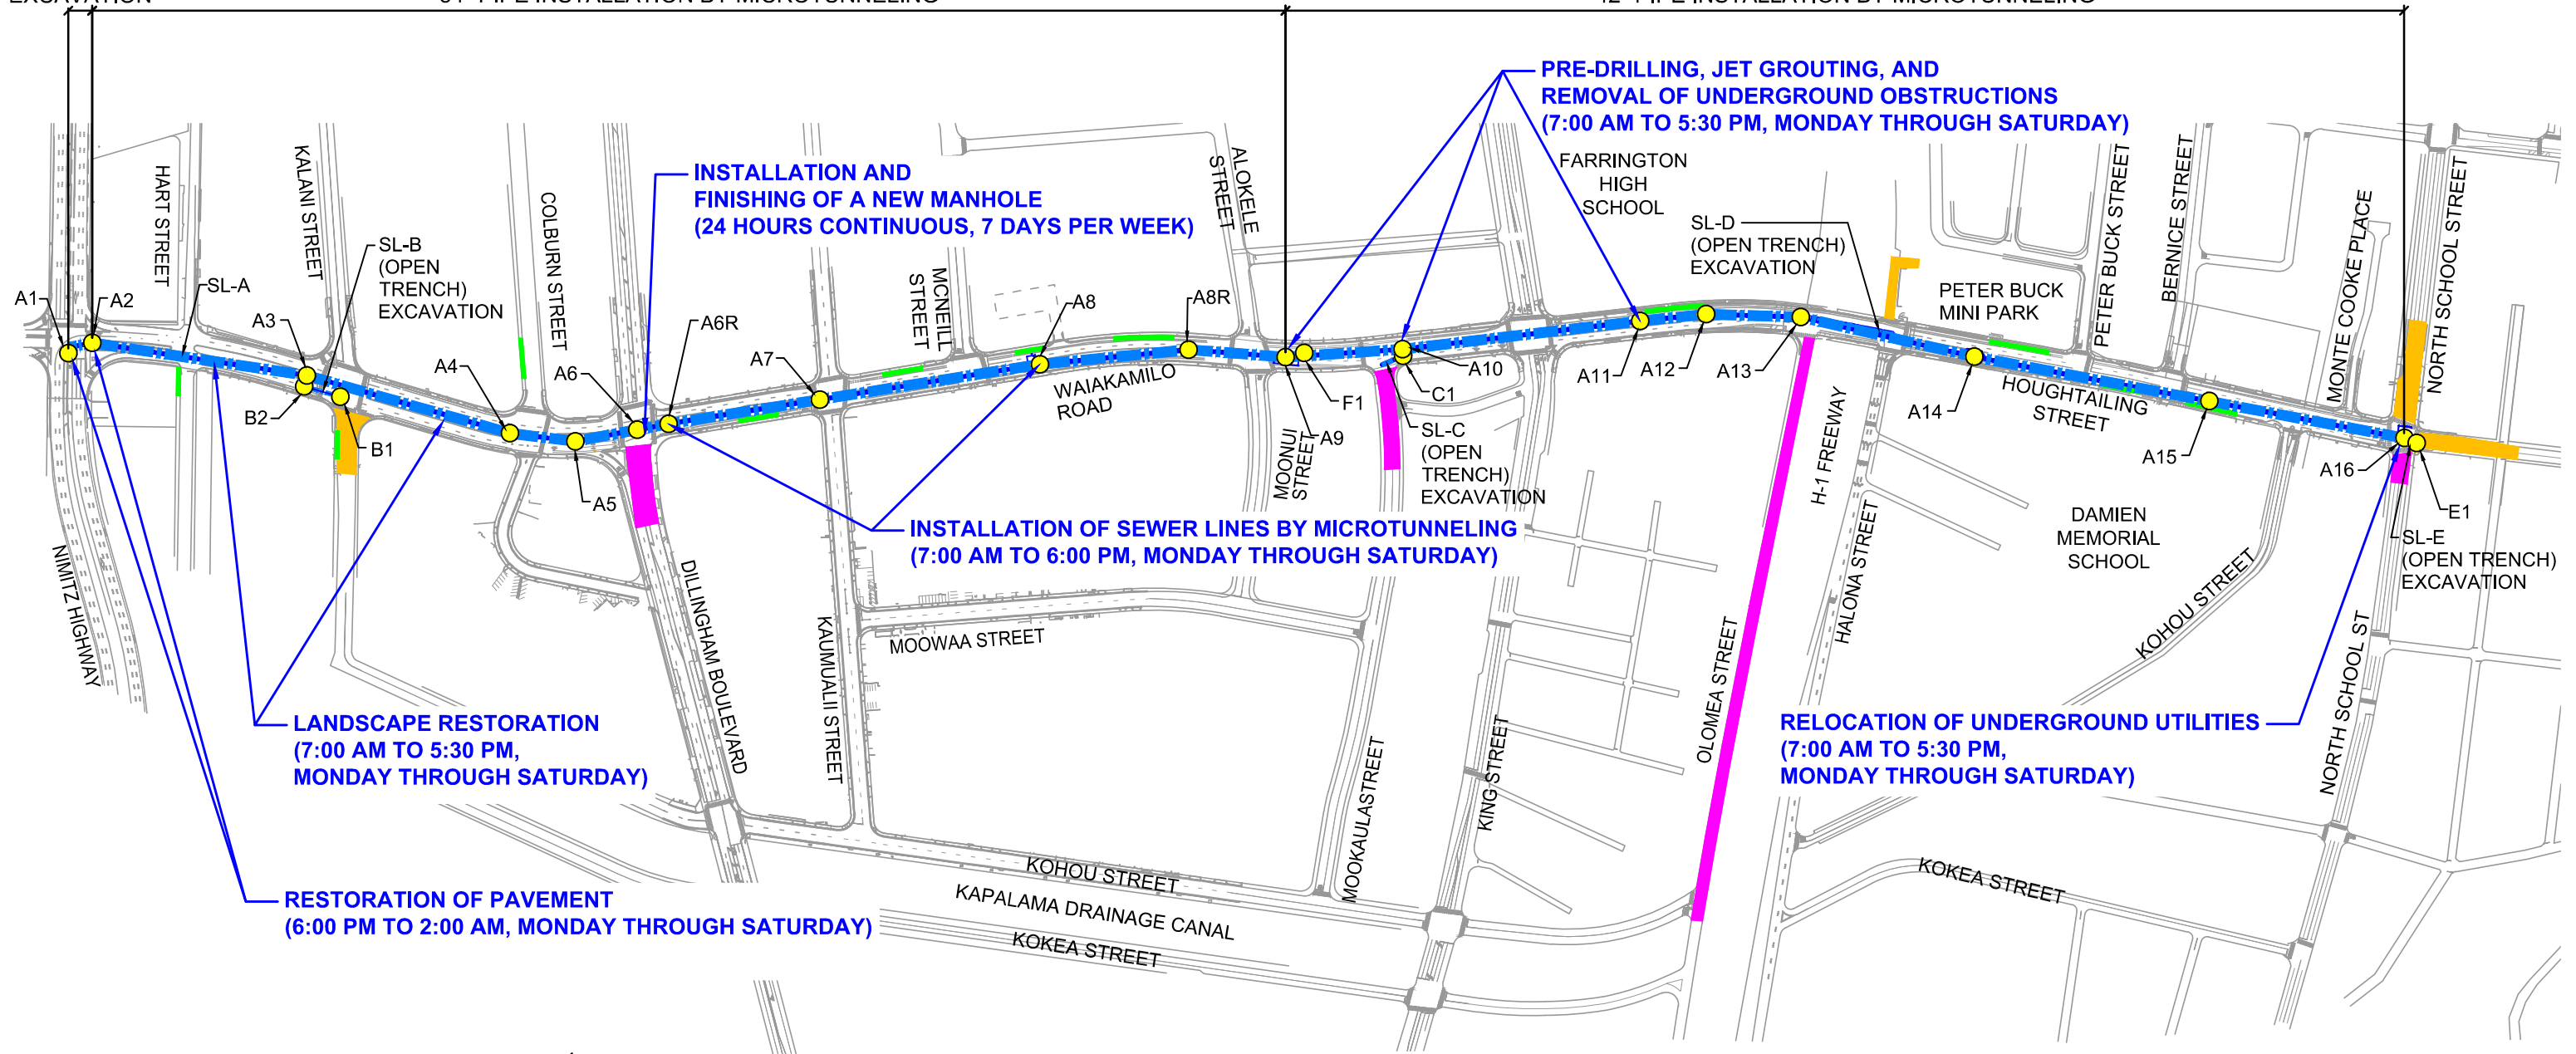

LANDSCAPE RESTORATION
(7:00 AM TO 5:30 PM, MONDAY THROUGH SATURDAY)


RESTORATION OF PAVEMENT
(6:00 PM TO 2:00 AM, MONDAY THROUGH SATURDAY)

INSTALLATION AND FINISHING OF A NEW MANHOLE
(24 HOURS CONTINUOUS, 7 DAYS PER WEEK)


INSTALLATION OF SEWER LINES BY MICROTUNNELING
(7:00 AM TO 6:00 PM, MONDAY THROUGH SATURDAY)

PRE-DRILLING, JET GROUTING, AND REMOVAL OF UNDERGROUND OBSTRUCTIONS
(7:00 AM TO 5:30 PM, MONDAY THROUGH SATURDAY)

RELOCATION OF UNDERGROUND UTILITIES
(7:00 AM TO 5:30 PM, MONDAY THROUGH SATURDAY)



- LEGEND:
- NEW SEWER MANHOLE
 - ▬▬▬ NEW SEWER LINE
 - ▬▬▬ ABANDONED SEWER MANHOLE AND SEWER LINE WORK AREA
 - ▬▬▬ TEMPORARY EQUIPMENT STORAGE AREA
 - ▬▬▬ TEMPORARY BYPASS WORK AREA



CITY AND COUNTY OF HONOLULU
DEPARTMENT OF ENVIRONMENTAL SERVICES

**AWA STREET WASTEWATER PUMP STATION
FORCE MAIN AND SEWER SYSTEM IMPROVEMENTS
WAIAKAMILO ROAD TRUNK SEWER, C&C JOB NO. W5-16**
